


Measure A Modernization Update (and other projects)

Presented to:

Bond Oversight Committee

January 13, 2015



Measure A Modernization Update

- **Projects Completed**
- **Projects in Progress**
- **Master Schedule**
- **Measure A Budget & Expenditures**
- **Non-Measure A Projects**
- **Projects in Planning**



MEASURE

A

School Bond

Measure A Projects Completed

- **Group I Underground Utilities (8 sites)**
- **Group II Modernization (6 Elem., 1 Int.)**
- **Group III Modernization (All 14 completed)**
 - ✓ Bryant, Clinton, Evans, Hazard, Lawrence
 - ✓ Marshall, Mitchell, Newhope, Peters, Rosita
 - ✓ Russell, Skylark, Warren, Zeyen
- **Group IV Modernization– (12 of 27 ES completed)**
 - ✓ Allen, Barker, Crosby, Eisenhower, Excelsior
 - ✓ Heritage, Morningside, Murdy, Northcutt
 - ✓ Riverdale, Violette, Woodbury



MEASURE

A

School Bond

Measure A Projects Completed

Group IV -

7 Active Construction Projects

Anthony

Carver

Cook

Gilbert

Parkview

Patton

Sunnyside



MEASURE

A

School Bond

Measure A Modernization Update

Anthony Elementary



Trenching for infrastructure



MEASURE

A

School Bond

Measure A Modernization Update

Anthony Elementary



New underground conduits for electrical service

MEASURE

A

School Bond

Measure A Modernization Update

Carver Elementary



Office relocation to front of campus for safety

MEASURE

A

School Bond

Measure A Modernization Update

Carver Elementary



Kinder class – sliding doors removed



Measure A Modernization Update

Cook Elementary



After modernization



MEASURE

A

School Bond

Measure A Modernization Update

Cook Elementary



Playground resurfaced



Measure A Modernization Update

Gilbert Elementary



Underground infrastructure




Measure A Modernization Update

Parkview Elementary



Preparation for flat work



Measure A Modernization Update

Patton Elementary



Office



MEASURE

A

School Bond

Measure A Modernization Update

Patton Elementary



Office



MEASURE

A

School Bond

Measure A Modernization Update

Sunnyside Elementary School



Finished Kinder Classroom

MEASURE

A

School Bond

Measure A Modernization Update

Sunnyside Elementary School



New windows



MEASURE

A

School Bond

Measure A Modernization Update

Sunnyside Elementary School



New windows



MEASURE

A

School Bond


Measure A Projects in Progress

- **Marquees**

- ✓ Crosby, Morningside, Parkview,
Sunnyside, Woodbury



Measure A Projects in Progress

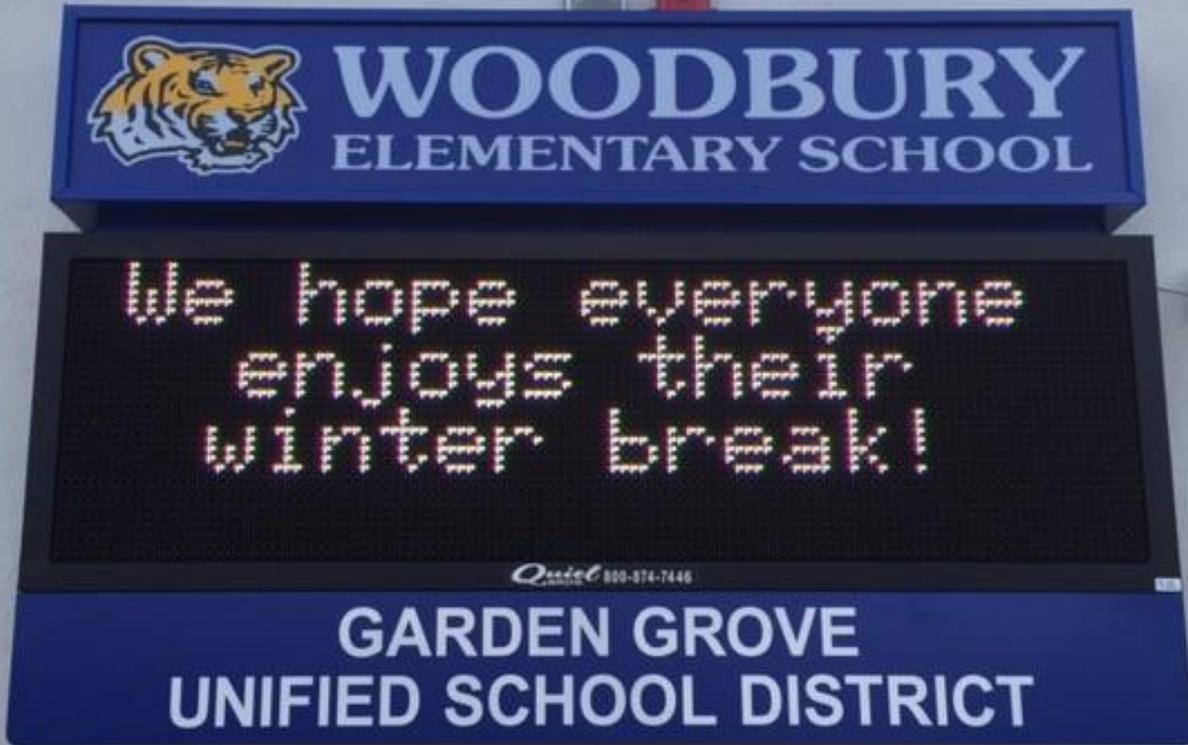

Measure A Projects in Progress



Measure A Projects Started December

■ **Group V – 4 Intermediates, 4 High Schools**

- ❖ Doig IS Classrooms
- ❖ Jordan IS Classrooms
- ❖ McGarvin IS Classrooms
- ❖ Walton IS Classrooms
- Garden Grove HS Classrooms
- La Quinta HS Admin
- Pacifica HS Admin
- Rancho HS Classrooms



MEASURE

A

School Bond

Measure A Modernization Update

Doig Intermediate



Typical demolition in classroom



Measure A Modernization Update

McGarvin Intermediate



Typical demolition in classroom



Walton Intermediate



Typical asbestos abatement containment



Garden Grove High



Electrical and low voltage conduits





Edison conduit encased in concrete slurry





Temporary path of travel



Pacifica High



Office gutted for grout injection – voluntary seismic mitigation



Pacifica High



Office gutted for grout injection – voluntary seismic mitigation





Core drilling for grout injection



Measure A Modernization Update

Rancho High



Demolition in typical classroom




Measure A Modernization Update

Rancho High

Underground utilities, hydroseed, new flagpole



Measure A Schedule

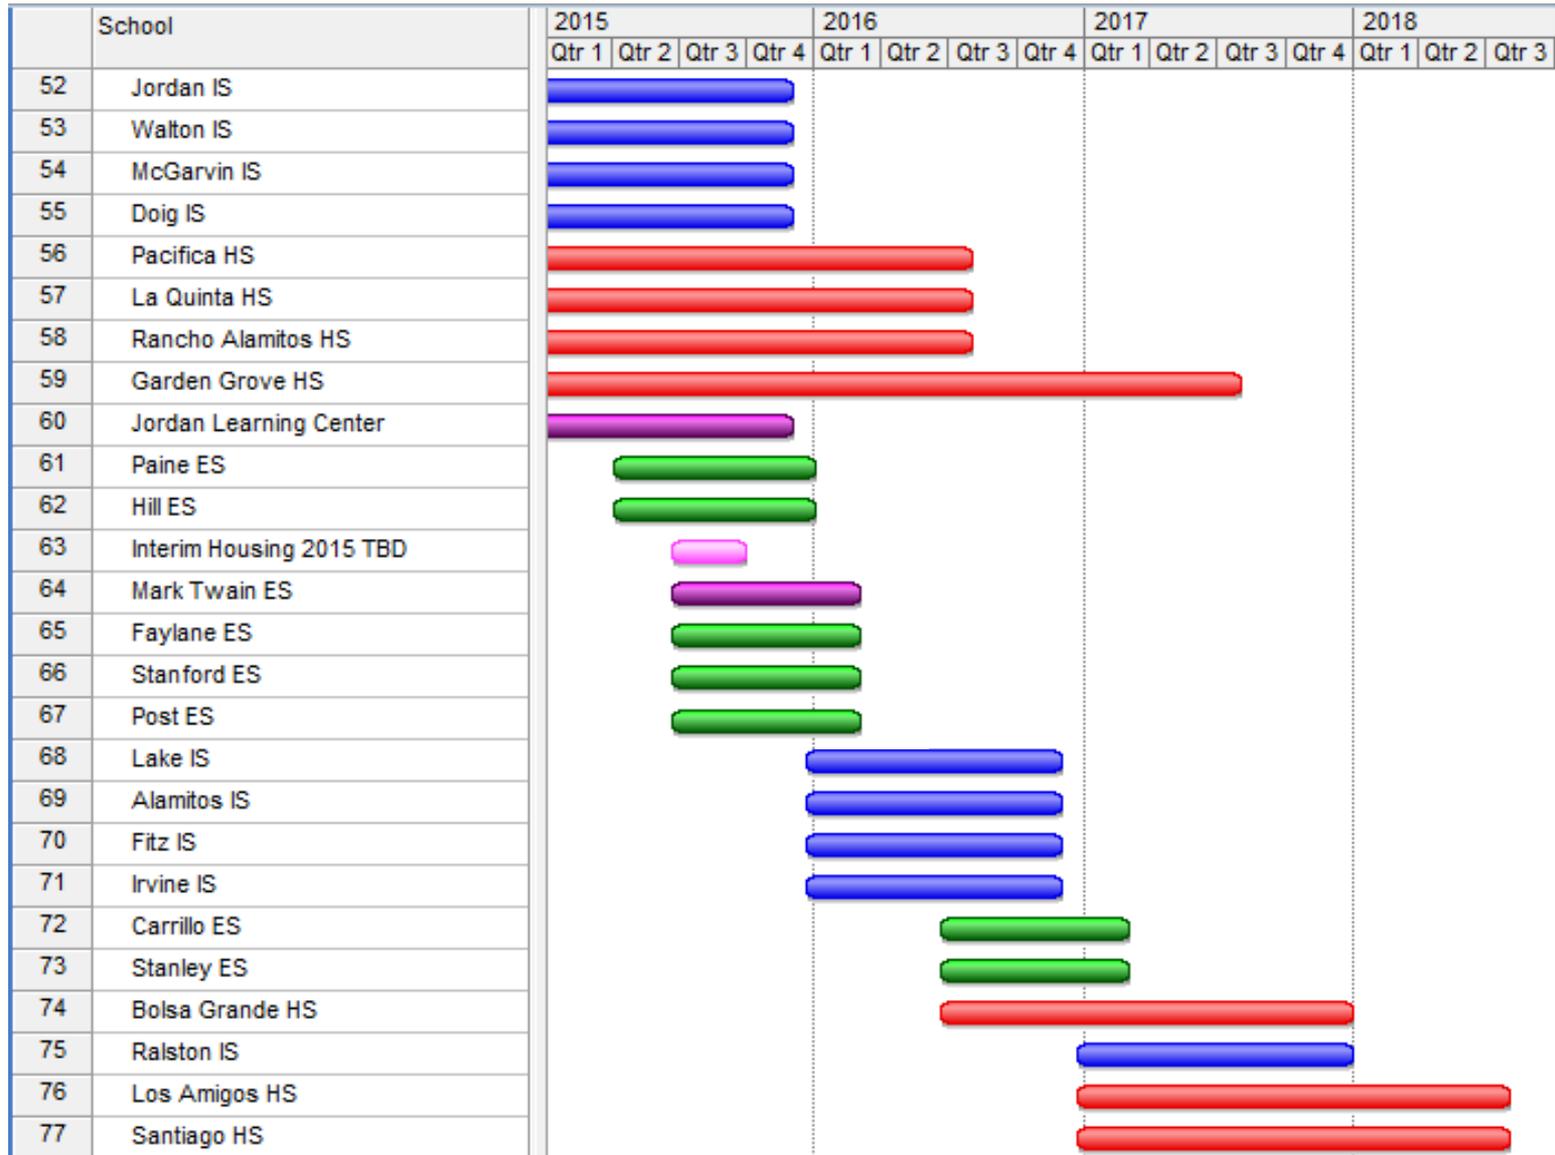

Measure A Expenditures

- **Committed Contracts**

 - \$ 417.9 million

 - \$ 354.2 million - Construction & Network/Data Upgrades

- **Expenditures to Date**

 - \$ 204.9 million

 - \$ 157.7 million - Construction & Network/Data Upgrades

- ❖ **Modernization Projects**

 - are on schedule and within the program budget

- ❖ **GGUSD has received 100% of State Modernization Funds \$253,688,639**



MEASURE

A

School Bond
